



ARCHITECTURAL OASIS CONTRACTING CO.

CR. 2051247508

شركة واحة المعمار للمقاولات .

سجل تجاري: 2051247508

AOC CONTRACTING COMPANY

Kingdom of Saudi Arabia

COMMERCIAL PROPOSAL

— FOR —

Construction of Razeen Al Seef Project

PRESENTED TO

RAZEEN REAL ESTATE COMPANY.

Proposal Reference	AOC-CO-260513R02	Date Issued	15/09/2026
Client RFQ / Tender No.	Email Dated 17.08.2026	Validity Period	30 days from issue date
Submitted By	AOC Contracting Company	Revision	Rev 1
Business Unit	<<Commercial & Industrial >>	Currency	Saudi Riyal (SAR)



Table of Contents

Letter to Client	3
1. Company Profile	4
2. Project Understanding	5
3. Scope of Work	6
4. Technical Approach & Methodology	7
5. Project Schedule	8
6. Organization & Key Personnel	9
7. HSE Management	10
8. Quality Assurance & Quality Control	11
9. Commercial Proposal	12
10. Terms & Conditions	13
11. Acceptance & Signature	14
12. Appendices	15



Letter to Client

15/09/2026

To:

Razeen Real Estate Company.

ATTENTION: Mr. Moustafa Eid

Kingdom of Saudi Arabia.

Subject: Commercial Proposal — **Construction of Razeen Al Seef Project**

Reference: **AOC-CO-260513R02** Dated **15/09/2026**

Dear Sir / Madam,

We are pleased to submit AOC Contracting Company's commercial proposal for the above-referenced project. Following our review of your enquiry documents and the site information made available, this proposal sets out our understanding of the scope, our proposed approach, the project organization, and our commercial offer.

AOC Contracting Company is a Saudi contracting firm established in 2021, delivering commercial & industrial across the Kingdom. We have built a track record of safe, on-time and on-budget project delivery, and we welcome the opportunity to support Razeen Real Estate Company

On this assignment.

Our proposal is open for acceptance for a period of Thirty (30) days from the date of this letter. We remain available to clarify any technical or commercial point and look forward to your favorable consideration.

Yours faithfully,



Abdulrahman Samir

Business Development Director

Architectural Oasis Contracting Co.

Email: << a.zitawi@aoc-sa.com>> · Mobile: <<+966 565584458>>



1. Company Profile

1.1 About AOC Contracting Company

AOC Contracting Company is a Saudi-based contracting firm founded in 2021, with a head office in Khobar, KSA. We deliver construction, fit-out and specialist works across two business units — Commercial & Industrial (operational since 2021) and Oil & Gas (launched 2026).

In FY2025 we achieved a turnover of SAR 65 million, executing projects for private developers, retail clients, industrial and warehouse owners. We employ a team of qualified project managers, engineers, planners, QA/QC and HSE professionals, supported by a centralized Finance, HR and Procurement function.

1.2 Vision & Values

- Vision: To be a trusted Saudi contractor delivering safe, high-quality industrial, commercial and oil & gas projects across the Kingdom.
- Values: Safety first · Quality without compromise · Integrity in dealings · Accountability for outcomes · Respect for people.

1.3 Core Capabilities

- Commercial buildings, retail fit-out, mixed-use developments.
- Industrial facilities: warehouses, factories, workshops, cold stores.
- Mechanical, Electrical & Plumbing (MEP) works.
- Oil & Gas: piping, mechanical, E&I, shutdowns, brownfield works, commissioning support.
- Civil works, structural concrete, steel structures.
- Project management, design coordination and turnkey solutions.
- In-house Steel Structure Design and Fabrication

1.4 Key Facts

Year Established	2021
CR No.	2051247508
VAT No.	311836796400003
FY25 Turnover	SAR 65 million
Headcount	71
Business Units	Commercial & Industrial · Oil & Gas
Certifications	ISO 9001:2015 & ISO 14001:2015



1.5 Selected Project Experience

#	Project	Client	Scope of work	Value (SAR)	Role
1	<i>Chedi Hegra Hotel</i>	<i>Craft</i>	<i>Turnkey</i>	<i>21M SAR</i>	<i>Sub-contractor</i>
2	<i>Zamil Food cold store</i>	<i>Zamil food</i>	<i>Turnkey</i>	<i>21.7M SAR</i>	<i>main contractor</i>
3	<i>USTS Facility</i>	<i>USTS</i>	<i>Turnkey</i>	<i>13M SAR</i>	<i>main contractor</i>
4	<i>BIN Zager 1,2</i>	<i>BIN Zager</i>	<i>Turnkey</i>	<i>19.1M SAR</i>	<i>main contractor</i>
5	<i>NUPCO Warehouses</i>	<i>NUPCO</i>	<i>Turnkey</i>	<i>17.3M SAR</i>	<i>main contractor</i>
6	<i>Gulf season factory</i>	<i>Gulf season</i>	<i>Turnkey</i>	<i>4.7M SAR</i>	<i>main contractor</i>



2. Project Understanding

2.1 Project Background

We understand that **RAZEEN REAL ESTATE COMPANY**. Intends to **Razeen al seef commercial building** at **Dhahran, KSA**.

2.2 Project Objectives

Based on the enquiry documents, AOC understands the principal objectives of the project to be:

- **complete the work within 10 months.**

2.3 Critical Success Factors

- Safe execution with Zero Lost-Time Incidents (LTI).
- Delivery of the works on schedule, with strict control of mobilization, procurement and site activities.
- Compliance with client specifications, project standards, and applicable KSA regulations.
- Effective coordination with client, consultants, third-party inspectors and adjacent contractors.
- Quality of workmanship and materials, with documented QA/QC at every stage.

2.4 Key Assumptions in This Proposal

- Access to the site is available on the agreed mobilization date and unobstructed for the duration of the works.
- Utilities (power, water) are made available at the site boundary by the client.
- Required permits, NOCs and approvals are obtained by the client unless specifically listed in our scope.
- Site conditions are as represented in the tender documents; latent or undisclosed conditions are excluded from this fixed price.



3. Scope of Work

3.1 Scope Summary

AOC's scope under this proposal comprises

1. *Civil structural work*
2. *Architectural work*
3. *Mechanical work*
4. *Electrical work*

3.2 Detailed Inclusions

The following items are INCLUDED on our price:

- *Civil works: (excavation, foundations, columns, SOG, UG tanks & all site works)*
- *structural steel: (supply, fabrication, erection.)*
- *Mechanical work: (Plumbing, HVAC, Firefighting).*
- *Electrical work: (Transformers, Panel boards, low voltage cables, Lightings, Earthing & fire alarm works).*

3.3 Exclusions

The following items are EXCLUDED from our price unless specifically agreed in writing:

- *All government permits or site permits.*
- *Dewatering*
- *Supply of steel structure work and sandwich panels*
- *Internal block*
- *Internal finishes*
- *Sanitary fixtures*
- *HVAC*
- *Internal MEP work*

3.4 Conditions

- *Our price is limited to 2.5 m excavation, 1.5 m soil replacement, non-UL firefighting system*

3.4 Deliverables

- Approved shop drawings and material submittals.
- Quality records: ITP results, material test certificates, NCR register.
- Daily / weekly progress reports.
- As-built drawings and operation & maintenance manuals at handover.
- Final take-over certificate and signed snag-list close-out.



4. Technical Approach & Methodology

4.1 Execution Philosophy

AOC will deliver the works in clearly defined phases, with dedicated review gates between each phase. The overall delivery model is single-source responsibility through a dedicated project team led by an experienced Project Manager.

4.2 Phases of Work

Phase	Key Activities	Deliverables
1. Mobilization	Contract signing, kick-off meeting, site set-up, HSE plan, programmed baseline, submittal schedule.	Mobilization plan, baseline schedule, project HSE plan, organization chart.
2. Engineering & Submittals	Shop drawings, material submittals, samples, method statements, ITPs.	Approved drawings & submittals, ITPs, method statements.
3. Procurement	Material orders, factory acceptance tests where applicable, expediting, logistics.	PO log, FAT certificates, delivery schedule.
4. Construction	Civil / structural / MEP / finishing works as per approved drawings, with progressive QA/QC and HSE oversight.	Daily/weekly reports, ITP records, NCR register, photographs.
5. Testing & Commissioning	System testing, balancing, performance verification, snag-list resolution.	Test certificates, commissioning report.
6. Handover & Close-out	Final inspection, as-built drawings, O&M manuals, training, taking-over certificate.	As-builts, O&M manuals, taking-over certificate, defects-liability declaration.

4.3 Standards & Codes

All works will be carried out in accordance with the following standards as applicable:

- Saudi Building Code (SBC) and relevant municipal regulations.
- Project specifications and approved drawings.
- AOC HSE Management System and project HSE Plan.
- AOC Quality Management System (ISO 9001 aligned) and project Quality Plan.



5. Project Schedule

Total project duration — **10** calendar months from the date of contract signature, subject to receipt of client approvals on schedule.

5.1 Key Milestones

#	Milestone	Target Date / Week
M1	Contract Signature	1st month
M2	Mobilization Complete	1st month
M3	All Submittals Approved	2nd month
M4	Procurement Complete	3th month
M5	Civil Works Complete	6th month
M6	MEP Works Complete	9th month
M7	Testing & Commissioning Complete	10th month
M8	Handover / Taking-Over Certificate	10th month

5.2 Schedule Assumptions


- Client approvals (drawings, submittals, samples, variations) returned within 7 calendar days.
- Continuous site access during normal working hours; nightshift / holiday working as agreed.
- No suspension of work due to events outside AOC's control (Force Majeure, client delays, regulatory holds).
- All free-issue items by client delivered to site by their scheduled dates.



6. Organization & Key Personnel

A dedicated project team will be assigned to this project, supported by AOC's central resources in Finance, HR, Procurement, QA/QC and HSE.

6.1 Project Organization Chart

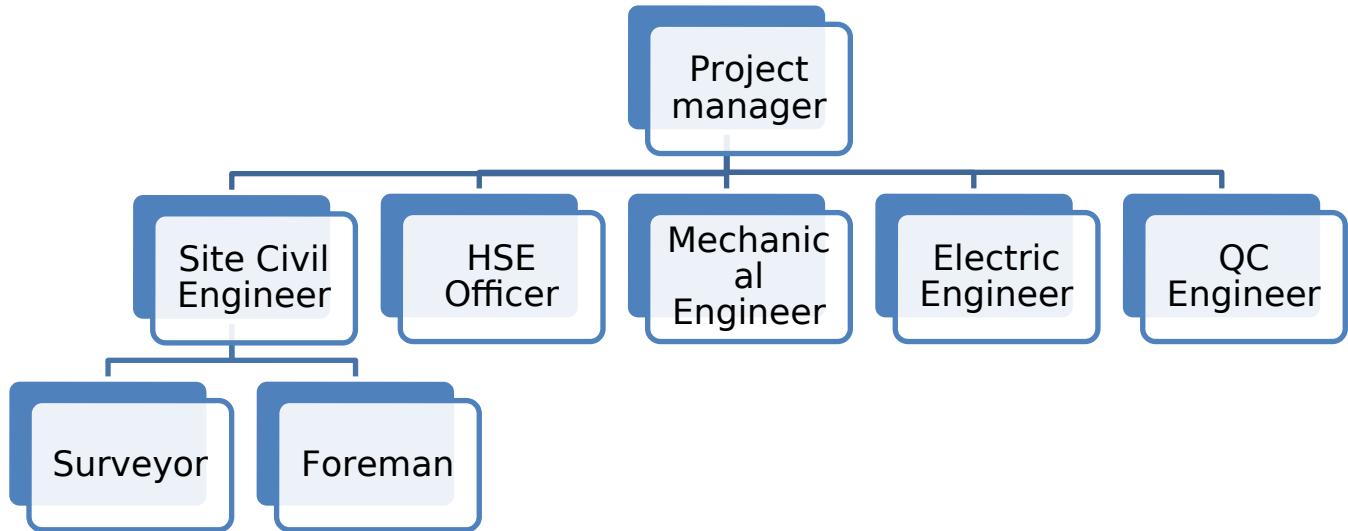



7. HSE Management

7.1 HSE Policy

AOC operates a Zero-Harm policy. Every project is delivered under a project-specific HSE Plan, with a dedicated HSE Manager / Officer on site always. We work towards a Lost-Time Incident Frequency Rate (LTIFR) of zero across all our projects.

7.2 HSE Approach for This Project

- Project HSE plan approved by client before mobilization.
- Permit-to-Work (PTW) system enforced for hot work, confined space, working at heights, energized electrical work, and lifting operations.
- Daily Toolbox Talks and weekly safety stand-downs.
- Mandatory PPE; site induction for all personnel before access.
- Monthly HSE statistics report (man-hours, near misses, incidents, training).
- Emergency Response Plan with on-site first-aiders and evacuation drills.

7.3 HSE Targets for This Project

Metric	Target
Lost-Time Incidents (LTI)	Zero
Total Recordable Incident Rate (TRIR)	< 0.5
Near-Miss Reporting Rate	≥ 1.0 per 200,000 man-hours
Site Induction Coverage	100% before site access
PPE Compliance	100% on all active sites



8. Quality Assurance & Quality Control

8.1 Quality Management System

AOC's Quality Management System is aligned with ISO 9001:2015. For each project, a project-specific Quality Plan is developed and submitted to the client for approval before commencement of work.

8.2 Quality Approach for This Project

- Project Quality Plan approved by the client before mobilization.
- Inspection & Test Plans (ITPs) for each work package.
- Material Approval Requests (MARs) and shop-drawing submittals.
- Third-party inspection where required by specification.
- Non-Conformance Reports (NCRs) issued and tracked to closure.
- Quality records retained for the project DLP and beyond as required.

8.3 Document Control

All project documents are managed through AOC's Electronic Document Management System with controlled revisions, approval workflows and a complete audit trail.



9. Commercial Proposal

9.1 Lump Sum Price

AOC's LUMP SUM PRICE for the scope of work defined in Section 3 is: **SAR 11,011,000**

(eleven million and eleven thousand Saudi Riyals only) — exclusive of VAT.

9.2 Price Breakdown

Item	Description	Unit	Quantity	Amount (SAR)
1	Building A	LS	1	5,452,445.00
2	Building B	LS	1	5,558,555.00
Subtotal (excluding VAT)				11,011,000



9.3 Payment Terms

Mobilization Advance	20% of Contract Value, against Advance Payment Guarantee
-----------------------------	--

Progress Payments	Monthly, against measured progress certified by the client / consultant
Recovery of Advance	Pro-rata from each progress payment, fully recovered by 70% completion
Retention	10% from each invoice — half released at takeover, balance at end of DLP
Payment Period	From 3:7 days from invoice approval
Performance Bond	5% of Contract Value, valid through DLP
Defects Liability Period (DLP)	12 months since the initial handing over certificate
Long lead items	1. 30 % with PO approval from the supplier. 2. 20% with the payment. 3. 20% with delivery. 4. 30% according to progress.



10. Commercial Terms & Conditions

10.1 Proposal Validity

This proposal is valid for THIRTY (30) calendar days from the date of submission. Beyond this period, the prices, terms and schedule are subject to AOC's written confirmation or revision.

10.2 Currency

All prices in this proposal are quoted in Saudi Riyals (SAR). Foreign currency conversions, if any, are based on the exchange rate prevailing on the date of submission.

10.3 Taxes

All prices are exclusive of Value-Added Tax (VAT). VAT will be charged at the rate applicable on the date of each invoice. Any Zakat or income tax payable by AOC under KSA law is included in our prices.

10.4 Variations

Variations to the scope of work shall be agreed in writing before execution. Variations will be priced using the unit rates in this proposal, where applicable, or by fair valuation in line with industry norms. No work shall be carried out without the client's written instruction.

10.5 Liquidated Damages

Liquidated damages (LDs) for delay, if any, are limited to **<<5%>>** of the Contract Value per week of delay, with a maximum aggregate of **<<10%>>** of the Contract Value. LDs are AOC's sole and exclusive liability for delay; consequential, indirect and special damages are excluded.

10.6 Force Majeure

Neither party shall be liable for failure to perform any obligation under the contract arising from causes beyond its reasonable control, including but not limited to acts of God, war, civil unrest, government action, epidemics, or any other event customarily recognized as Force Majeure. The affected party shall give prompt written notice and use reasonable efforts to mitigate the impact.

10.7 Insurance

AOC will maintain Contractor's All-Risk (CAR), Third-Party Liability, and Workmen's Compensation insurance for the duration of the works. Copies of policies will be made available to the client upon request.

10.8 Governing Law & Disputes

This proposal, and any contract arising therefrom, shall be governed by and construed in accordance with the laws of the Kingdom of Saudi Arabia. Disputes shall first be resolved through good-faith negotiation and, failing that, referred to arbitration in Riyadh under the Saudi Center for Commercial Arbitration (SCCA) rules.



10.9 Confidentiality

All commercial, technical and pricing information contained in this proposal is confidential to **RAZEEN REAL ESTATE COMPANY**. And AOC. It shall not be disclosed to any third party without the prior written consent of both parties, except as required by law or regulatory authority.

10.10 Ownership of Documents

All drawings, calculations, methodologies, models and other documents prepared by AOC remain the intellectual property of AOC until full payment is received, at which point usage rights pass to the client for the purposes of the project.

11. Acceptance & Signature

This proposal becomes a binding commitment between AOC Contracting Company and RAZEEN REAL ESTATE COMPANY. upon the client's acceptance, evidenced by either (a) signature of this proposal in space below and return to AOC, or (b) issuance of a Letter of Award / Purchase Order referencing this proposal.

Submitted on behalf of AOC Contracting Company:

Abdulrahman Samir
Business Development Director
AOC Contracting Company

Signature: _____

Date: 15/09/2026

Stamp:



Accepted on behalf of **RAZEEN REAL ESTATE COMPANY**.

Name: _____

Title: _____

Signature: _____

Date: _____

Stamp: _____
